


Chapter IV

Project Implementation/Progress

2025-2028 Transportation Improvement Program

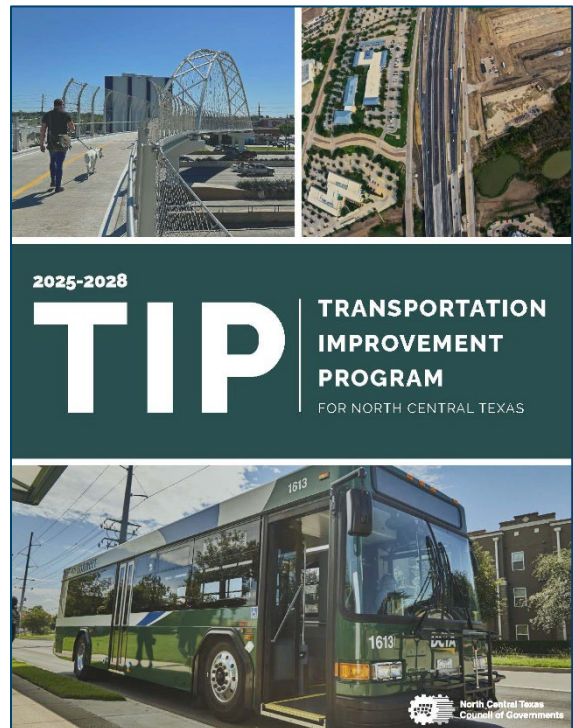

Chapter IV

Project Implementation/Progress from Previous Years

PROJECT LIST OVERVIEW

Section 450.326(n)(2) of Metropolitan Planning Rules requires that the Transportation Improvement Program (TIP) contain a list of major projects from the previous TIP that were implemented, as well as projects that experienced significant delays in their planned implementation. The Infrastructure Investment and Jobs Act (IIJA) emphasizes the TIP as a management tool for monitoring progress in implementation of the Metropolitan Transportation Plan (MTP). This chapter highlights the major projects implemented over the last three years, as well as projects delayed or cancelled during the same time frame. For purposes of this requirement, the Dallas-Fort Worth (DFW) Metropolitan Planning Organization (MPO) has defined major projects as those with construction funding over \$10 million. Projects were generally delayed due to funding constraints or project-specific issues such as right-of-way availability, utility relocation delays, environmental concerns, financial limitations, local government priorities, or design changes.

PROJECT IMPLEMENTATION

During the development of the 2025-2028 TIP, the Regional Transportation Council (RTC) made a strong commitment to implement projects that are listed in the TIP and the State Implementation Plan (SIP). NCTCOG staff is actively monitoring progress to ensure that RTC-selected projects are being implemented in a timely manner.

One of the ways that the RTC has attempted to ensure that projects are advancing in a timely manner is through approval of the MPO Milestone Policy. Through two rounds of this initiative, staff identified projects that were funded in 2010 or earlier and had not proceeded to construction. New deadlines for projects to go to construction by were approved by the RTC. If construction does not begin by the agreed upon deadline, funding will be removed from the project and returned to the regional pool for use on other projects. Of the 57 projects identified on the initial Milestone Policy list that were funded in 2006 or earlier, all have



Dynamic Message Signs provide travel-time estimates and other information to improve commutes.

advanced to construction or were canceled at the request of the project sponsor. A second round of the MPO Milestone Policy initiative is underway for projects funded between 2006 and 2010 that have not proceeded to construction. Of the 41 projects identified in that round, 20 have advanced to construction, 13 have been canceled at the request of the project sponsor, and 8 will continue to be monitored.

In addition to the Milestone Policy, a project tracking initiative has been implemented by staff to monitor project implementation more closely. This initiative is intended to help identify potential issues that may delay projects earlier in the process to prevent them from causing delays of ten or more years. It also aims to reduce the amount of funds that carry over from one fiscal year to the next. The focus of this effort is on three RTC-selected funding categories: Congestion Mitigation and Air Quality Improvement Program, Surface Transportation Block Grant, and Transportation Alternatives Set-Aside. A list with all project phases funded with those sources that are anticipated to obligate in a given fiscal year is generated at the beginning of the year and periodic updates on the status of those projects are brought to the Surface Transportation Technical Committee and the RTC throughout the year.

The tables included in this chapter summarize the major projects for which construction or implementation has begun, is in process, or has been completed in the Dallas and Paris districts (Eastern Subregion) and Fort Worth district (Western Subregion) of the Texas Department of Transportation (TxDOT) from FY2022 to FY2024, as well as any delays from original project scheduling. It is important to note that the Federal Highway Administration implements federal projects through TxDOT, while the Federal Transit Administration (FTA) implements projects directly through designated recipients or grantees, identified as “implementing agencies” in the following tables.

The 2023-2026 TIP, as originally submitted, contained 385 projects. Over the course of the past two years, 183 projects were added through quarterly TIP modification cycles. Of these, 182 are classified as “major projects.” Since the 2023-2026 TIP was initiated, construction started on 27 major projects. Engineering, environmental clearance, right-of-way acquisition, or utility relocation are underway for a significant number of these projects.

ROADWAY SECTION PROJECTS

Lists of projects from the roadway section of the TIP that were delayed, let, and/or completed are found in the exhibits as follows:

- Exhibit IV-1: TxDOT Fort Worth District
- Exhibit IV-2: TxDOT Dallas District
- Exhibit IV-3: TxDOT Paris District

The information provided for each project in these exhibits includes:

- original CSJ number (e.g., TxDOT project number)

- revised CSJ number (as appropriate)
- agency implementing the project
- TIP code (i.e., MPO project number)
- project location including project limits (i.e., from and to)
- project type
- original start date (date originally estimated for construction or implementation to be initiated)
- revised start date (if applicable)
- whether the project was let, completed, delayed, or cancelled since the last TIP was submitted, as applicable.


TRANSIT SECTION PROJECTS

Transit section projects are summarized differently than roadway section projects because the FTA implements projects in a different manner. Instead of “letting” like roadway section projects, once a transit project is included in an approved FTA grant for a particular fiscal year, it is incorporated into the relevant agency’s operating budget and proceeds toward implementation. A list of projects included in FY2022 through FY2024 grant applications to date is provided in Exhibit IV-4 for the Fort Worth District and in Exhibit IV-5 for the Dallas District. Transit projects included in the Paris District are administered by TxDOT and can be found in the Statewide Transportation Improvement Program.



Chapter IV Project Implementation/Progress from Previous Years

Roadway – Fort Worth District

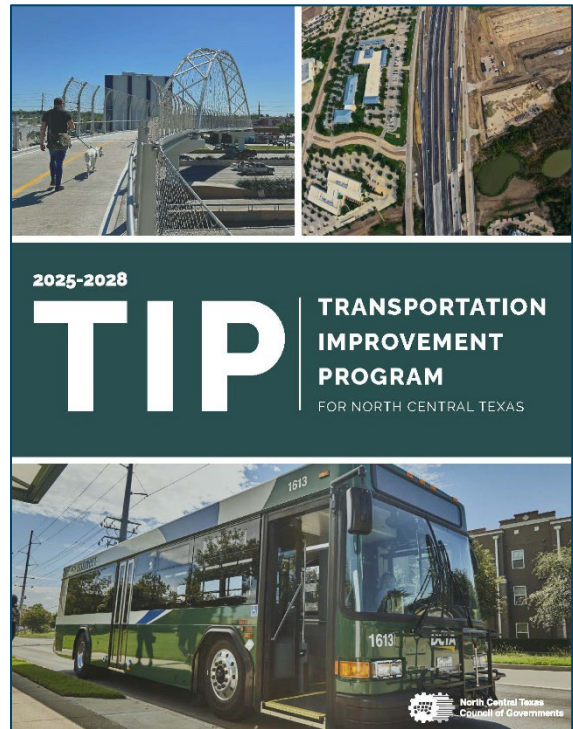

**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0902-90-228	0902-90-228	ARLINGTON	21064	CS From: ON CENTER STREET/MLK JR BLVD FROM BARDIN ROAD To: SE GREEN OAKS BOULEVARD	BIKE/PEDESTRIAN, NEW ROADWAY, TRAFFIC SIGNAL IMPROVEMENT	10/2024	10/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0902-90-034	0902-90-034	DFW AIRPORT	11734	CS From: EAST-WEST CONNECTOR FROM SH 360 To: INTERNATIONAL PARKWAY	NEW ROADWAY	03/2023	03/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0902-90-172	0902-90-172	FORT WORTH	25013	CS From: MEANDERING ROAD FROM SH 183 TO ANAHUAC AVE To: LTJG BARNETT FROM MEANDERING ROAD TO NASJRB EAST GATE	BIKE/PEDESTRIAN, INTERSECTION IMPROVEMENT, RECONSTRUCTION	09/2023	09/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0000-02-059	0000-02-059	FORT WORTH	84163	CS From: ON EVERMAN PARKWAY; FROM ROSEDALE SPRINGS LANE To: CAMERON HILLS POINT	NEW ROADWAY, BICYCLE/PEDESTRIAN, GRADE SEPARATION	10/2024	06/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0000-02-060	0000-02-060	FORT WORTH	84164	CS From: ON INTERMODAL PARKWAY; FROM BNSF RAILWAY To: OLD FM 156	ADDITION OF LANES, BIKE/PEDESTRIAN	07/2023	06/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0902-90-148	0902-90-148	FORT WORTH	14054	CS From: HORNE STREET FROM VICKERY BLVD To: CAMP BOWIE BLVD	ADDITION OF LANES, BIKE/PEDESTRIAN, TRAFFIC SIGNAL IMPROVEMENT	01/2025	05/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0902-90-343	0902-90-343	FORT WORTH	14054	CS From: HORNE STREET FROM VICKERY BLVD To: CAMP BOWIE BLVD	ADDITION OF LANES, BIKE/PEDESTRIAN, TRAFFIC SIGNAL IMPROVEMENT	01/2025	05/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0902-00-297	0902-00-297	FWTA	14090.1	IH 35W From: DR. DENNIS DUNKINS TRANSFER CENTER To: ALLIANCE	BUS TRANSIT	12/2022	10/2021	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0902-00-365	0902-00-365	FWTA	14090.1	IH 35W From: DR. DENNIS DUNKINS TRANSFER CENTER To: ALLIANCE	BUS TRANSIT	12/2022	10/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0902-90-304	0902-90-304	FWTA	14078	VA From: TRE STATION AT TRINITY LAKES To:	BUS TRANSIT, RAIL TRANSIT	02/2020	08/2023	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0902-90-303	0902-90-303	FWTA	11543.4	VA From: TEXRAIL EXTENSION PROJECT FROM FORT WORTH T&P STATION To: MEDICAL DISTRICT	RAIL TRANSIT	09/2023	09/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0902-90-206	0902-90-206	NTTA	21021	MH From: ON CHISHOLM TRAIL PARKWAY To: AT WORTH CREEK PARKWAY	INTERCHANGE	09/2024	01/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0000-02-052	0000-02-052	NTTA	84158	MH From: ON CHISHOLM TRAIL PARKWAY FROM FM 1187 To: US 67	NEW ROADWAY	01/2026	01/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0902-38-140	0902-38-140	PARKER CO	21006	CS From: ON OLD WEATHERFORD RD FROM FM 3325 To: E OF CODER DR.	REHABILITATION	06/2022	03/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE		PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0902-90-176	0902-90-176	TXDOT-FORT WORTH	14088	CS	From: ON LAS VEGAS TRAIL FROM QUEBEC DRIVE To: IH 820	ADDITION OF LANES, BIKE/PEDESTRIAN, INTERSECTION IMPROVEMENT, RECONSTRUCTION	01/2025	05/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0902-48-579	0902-48-579	TXDOT-FORT WORTH	11572	CS	From: US 81/US 287 AT FM 3479/HARMON ROAD/NORTH TARRANT PARKWAY To:	INTERSECTION IMPROVEMENT, NEW ROADWAY	11/2023	04/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0747-05-035	0747-05-035	TXDOT-FORT WORTH	54053	FM 157	From: BU 287 P To: US 67	ADDITION OF LANES	01/2027	11/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2418-01-013	2418-01-013	TXDOT-FORT WORTH	13004.1	FM 1810	From: WEST OF CR 1170 To: INTERSECTION OF US 81/287 AT FM 1810	GRADE SEPARATION, INTERSECTION IMPROVEMENT	09/2027	10/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
1181-02-033	1181-02-033	TXDOT-FORT WORTH	11955.1	FM 917	From: WEST OF AVE F To: MAIN STREET	GRADE SEPARATION, INTERSECTION IMPROVEMENT	09/2026	09/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2374-05-093	2374-05-093	TXDOT-FORT WORTH	13027.2	IH 20	From: PARK SPRINGS BLVD To: DALLAS COUNTY LINE	ADDITION OF LANES, BOTTLENECK REMOVAL	09/2026	11/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0314-07-061	0314-07-061	TXDOT-FORT WORTH	13054	IH 20	From: FM 2552 To: BANKHEAD HIGHWAY	NEW ROADWAY	05/2029	05/2029	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0008-03-094	0008-03-094	TXDOT-FORT WORTH	13061	IH 20 From: IH 20/IH 30 SPLIT To: TARRANT/PARKER COUNTY LINE	BRIDGE, INTERCHANGE	05/2023	05/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0008-03-133	0008-03-133	TXDOT-FORT WORTH	13061.1	IH 20 From: FM 1187/FM 3325 To: IH 20/IH 30 SPLIT	BOTTLENECK REMOVAL, RECONSTRUCTION	10/2023	05/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0008-16-044	0008-16-044	TXDOT-FORT WORTH	13061.2	IH 20 From: TARRANT/PARKER COUNTY LINE To: MARKUM RANCH ROAD	INTERCHANGE	10/2023	05/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2374-05-066	2374-05-066	TXDOT-FORT WORTH	55043	IH 20 From: IH 820 To: LITTLE ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	08/2022	08/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0008-13-206	0008-13-206	TXDOT-FORT WORTH	55045	IH 20 From: IH 820/IH 20 INTERCHANGE To: FOREST HILL DR	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	08/2022	08/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
1068-05-014	1068-05-014	TXDOT-FORT WORTH	13062	IH 30 From: IH 20/IH 30 SPLIT To: TARRANT/PARKER COUNTY LINE	BOTTLENECK REMOVAL	01/2023	05/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
1068-01-214	1068-01-214	TXDOT-FORT WORTH	13003	IH 30 From: SS 580 (E OF LINKCREST DR) To: IH 820	ADDITION OF LANES, BOTTLENECK REMOVAL, INTERCHANGE, RECONSTRUCTION	03/2024	07/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
1068-02-147	1068-02-147	TXDOT-FORT WORTH	13001	IH 30 From: WEST OF COOPER ST To: DALLAS COUNTY LINE	ADDITION OF LANES	09/2027	06/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0014-03-088	0014-03-088	TXDOT-FORT WORTH	13046	IH 35W From: BETHESDA ROAD To: ASHER ROAD	INTERCHANGE, RECONSTRUCTION	05/2025	08/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0014-03-087	0014-03-087	TXDOT-FORT WORTH	25070	IH 35W From: IH 35W NB OVER BI 35V To:	GRADE SEPARATION	08/2022	08/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0008-13-125	0008-13-125	TXDOT-FORT WORTH	55041	IH 820 From: IH 20 To: RAMEY AVE	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	08/2022	02/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0008-13-248	0008-13-248	TXDOT-FORT WORTH	21022	IH 820 From: AT TRINITY RAILWAY EXPRESS (TRE) LINE FROM NORTH OF TRINITY BLVD To: SOUTH OF SH 10	RECONSTRUCTION	05/2023	05/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0008-14-138	0008-14-138	TXDOT-FORT WORTH	11251.2	IH 820 From: IH 35W To: SH 121/SH 183/SH 26	ADDITION OF LANES, HOV/MANAGED/EXPRESS, REHABILITATION	09/2023	12/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0008-13-250	0008-13-250	TXDOT-FORT WORTH	55041.1	IH 820 From: RAMEY AVE To: BRENTWOOD STAIR ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	03/2023	03/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION		PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0008-14-132	0008-14-132	TXDOT-FORT WORTH	13005.1	IH 820	From: NAVAHO TRAIL/CAHOBA DRIVE To: MARINE CREEK PARKWAY	BOTTLENECK REMOVAL	01/2028	01/2030	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0364-01-162	0364-01-162	TXDOT-FORT WORTH	53104	SH 121	From: IH 820 To: FM 157	ADDITION OF LANES, HOV/MANAGED/EXPRESS	06/2023	12/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0365-03-053	0365-03-053	TXDOT-FORT WORTH	55312	SH 171	From: US 377 To: SH 174	REHABILITATION	02/2025	02/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0019-01-146	0019-01-146	TXDOT-FORT WORTH	14063	SH 174	From: N OF ELK DR To: WICKER HILL RD	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	10/2023	06/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0094-05-070	0094-05-070	TXDOT-FORT WORTH	13064	SH 183	From: AT PUMPHREY To:	INTERSECTION IMPROVEMENT	01/2027	03/2029	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0094-01-032	0094-01-032	TXDOT-FORT WORTH	13066	SH 183	From: AT UPRR & UPRR SPUR To:	BRIDGE, GRADE SEPARATION, RAIL TRANSIT	01/2023	03/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0171-05-068	0171-05-068	TXDOT-FORT WORTH	13005	SH 199	From: NORTH OF AZLE AVENUE To: SOUTH OF IH 820	ADDITION OF LANES, BOTTLENECK REMOVAL, INTERCHANGE	01/2028	01/2030	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.


**EXHIBIT IV-1 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0171-05-094	0171-05-094	TXDOT-FORT WORTH	13037	SH 199 From: NORTH UNIVERSITY DRIVE/WEST NORTHSIDE DRIVE To: SOUTH OF IH 820	REHABILITATION	06/2026	09/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2266-02-148	2266-02-148	TXDOT-FORT WORTH	13008	SH 360 From: NORTH OF E RANDOL MILL RD To: SOUTH OF E RANDOL MILL RD	ADDITION OF LANES, BRIDGE, RAIL TRANSIT, RECONSTRUCTION	12/2026	12/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0172-09-028	0172-09-028	TXDOT-FORT WORTH	55042	US 287 From: IH 20 INTERCHANGE To: SUBLETT ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	08/2022	02/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0172-06-080	0172-06-080	TXDOT-FORT WORTH	55044	US 287 From: IH 820 To: VILLAGE CREEK ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN, RECONSTRUCTION	08/2022	02/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0013-07-083	0013-07-083	TXDOT-FORT WORTH	13004.2	US 81 From: NORTH OF CR 2195 To: NORTH OF US 380	ADDITION OF LANES, GRADE SEPARATION, INTERSECTION IMPROVEMENT	09/2027	10/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0014-15-034	0014-15-034	TXDOT-FORT WORTH	53030	US 81 From: NORTH OF HARMON ROAD To: NORTH OF IH 35W	REHABILITATION	11/2023	05/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0014-15-078	0014-15-078	TXDOT-FORT WORTH	13063	US 81/US 287 From: SOUTH OF NORTH TARRANT PARKWAY To: AVONDALE HASLET ROAD	BOTTLENECK REMOVAL, ADDITION OF LANES, BIKE/PEDESTRIAN	04/2029	04/2029	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

Chapter IV Project Implementation/Progress from Previous Years

Roadway – Dallas District

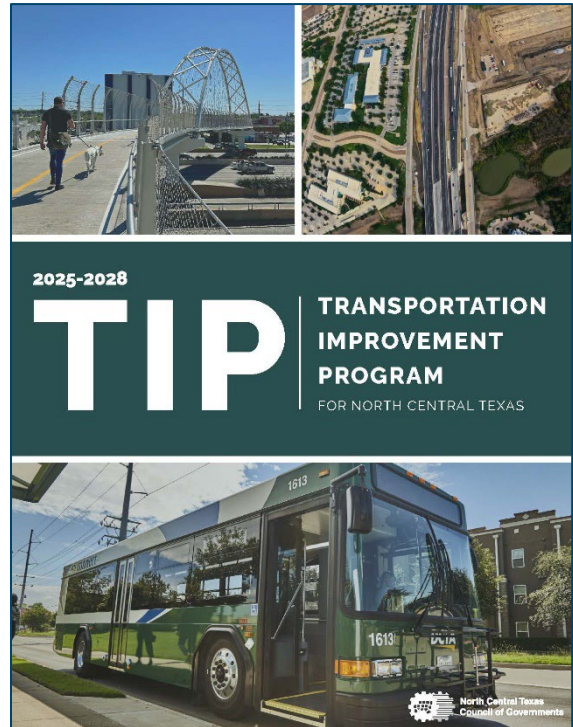

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE		PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0918-47-313	0918-47-313	BALCH SPRINGS	25078	CS	From: ON HICKORY TREE ROAD; FROM ELAM ROAD To: LAKE JUNE ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN	12/2024	10/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0000-18-115	0000-18-115	COLLIN CO	84160	MH	From: ON COLLIN COUNTY OUTER LOOP FROM FM 2478 To: US 75	NEW ROADWAY	11/2022	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-244	0918-47-244	DALLAS	14000	CS	From: ON PRAIRIE CREEK RD FROM N OF MILITARY PKWY To: NORTH OF FORNEY ROAD	GRADE SEPARATION	10/2023	01/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-286	0918-47-286	DALLAS	14046	VA	From: UPTOWN MCKINNEY/COLE COUplet: ON ALLEN ST FROM CARLISLE ST TO MCKINNEY AVE; ON CARLISLE ST FROM COLE AVE TO ALLEN ST; To: ON COLE AVE FROM HARVARD AVE TO CARLISLE ST; ON MCKINNEY AVE FROM HARVARD AVE TO ALLEN ST	RECONSTRUCTION, TRANSIT (GENERAL)	12/2022	01/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-474	0918-47-474	DALLAS	25107	VA	From: FIVE MILE CREEK AT WESTMORELAND DART STATION FROM ILLINOIS AVE TO WESTMORELAND AND To: FROM HAMPTON TO RUGGED DRIVE	BIKE/PEDESTRIAN	08/2025	06/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-296	0918-47-296	DALLAS	14085	VA	From: CIRCUIT TRAIL CONNECTOR/KATY TRAIL EXTENSION FROM KATY TRAIL To: TRINITY STRAND TRAIL	BIKE/PEDESTRIAN	06/2022	06/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0918-47-168	0918-47-168	DALLAS CO	11726.4	CS	From: RIVERFRONT BLVD FROM CADIZ STREET To: JUSTICE CENTER WAY	ADDITION OF LANES, BIKE/PEDESTRIAN, INTERSECTION IMPROVEMENT, RECONSTRUCTION	08/2022	12/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE		PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0918-47-208	0918-47-208	DALLAS CO	14002	CS	From: ON WINTERGREEN RD FROM JEFFERSON STREET To: WEST OF CARPENTER ROAD	ADDITION OF LANES, RECONSTRUCTION	09/2025	11/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-239	0918-47-239	DALLAS CO	14003	CS	From: JEFFERSON ST FROM WINTERGREEN RD TO PLEASANT RUN RD AND PLEASANT RUN RD FROM JEFFERSON ST To: LANCASTER-HUTCHINS RD	ADDITION OF LANES, RECONSTRUCTION	09/2025	01/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-00-427	0918-00-427	DART	14013.7	VA	From: COTTON BELT VELOWEB TRAIL FROM DFW AIRPORT NORTH COTTON BELT STATION To: SHILOH COTTON BELT STATION	BIKE/PEDESTRIAN	11/2023	10/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-00-428	0918-00-428	DART	14013.8	VA	From: COTTON BELT VELOWEB TRAIL FROM DFW AIRPORT NORTH COTTON BELT STATION To: SHILOH COTTON BELT STATION	BIKE/PEDESTRIAN	11/2023	10/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-00-469	0918-00-469	DART	24013	VA	From: TRE REPLACEMENT VEHICLES To:	RAIL TRANSIT	03/2024	09/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-510	0918-47-510	DART	14073.2	VA	From: COTTON BELT VELOWEB TRAIL FROM EAST OF SURVEYOR BLVD To: PGBT IN PLANO	BIKE/PEDESTRIAN	03/2024	06/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-00-388	0918-00-388	DART	25097	VA	From: SILVER LINE FROM DFW AIRPORT STATION To: SHILOH STATION IN PLANO	RAIL TRANSIT	12/2022	08/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE		PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0918-47-478	0918-47-478	DART	25097.1	VA	From: SILVER LINE FROM DFW AIRPORT STATION To: SHILOH STATION IN PLANO	RAIL TRANSIT	11/2023	01/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-480	0918-47-480	DART	25097.2	VA	From: SILVER LINE FROM DFW AIRPORT STATION To: SHILOH STATION IN PLANO	RAIL TRANSIT	11/2023	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-481	0918-47-481	DART	25097.4	VA	From: ON A TRAIN RAIL LINE FROM THE DOWNTOWN CARROLLTON STATION To: TRINITY MILLS STATION	RAIL TRANSIT	08/2024	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-462	0918-47-462	DART	25105	VA	From: SILVER LINE FROM DFW AIRPORT STATION To: SHILOH STATION IN PLANO	OTHER	10/2023	08/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0918-00-337	0918-00-337	DART	14013.2	VA	From: COTTON BELT VELOWEB TRAIL FROM DFW AIRPORT NORTH COTTON BELT STATION To: SHILOH COTTON BELT STATION	BIKE/PEDESTRIAN	07/2022	05/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-48-004	0918-48-004	DART	14013.2	VA	From: COTTON BELT VELOWEB TRAIL FROM DFW AIRPORT NORTH COTTON BELT STATION To: SHILOH COTTON BELT STATION	BIKE/PEDESTRIAN	07/2022	12/2021	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0918-46-319	0918-46-319	DENTON	14074	CS	From: BONNIE BRAE STREET FROM WINDSOR DRIVE To: US 77	ADDITION OF LANES, BIKE/PEDESTRIAN	11/2022	05/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE		PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0918-46-352	0918-46-352	DENTON	40052	VA	From: PECAN CREEK TRAIL FROM LAKEY ST AT WILSON ST TO S WOODROW LN AND To: FROM SL 288 TO GLENNGARY WAY & E MCKINNEY ST	BIKE/PEDESTRIAN	08/2025	08/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0918-46-316	0918-46-316	DENTON CO	14033	CS	From: ON SOUTH SHADY SHORES ROAD FROM WEST SHADY SHORES ROAD TO OAKWOOD CIRCLE AND FROM PARKSIDE LANE To: SILKTREE COURT	RECONSTRUCTION	12/2023	09/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-24-207	0918-24-207	FRISCO	20277.1	CS	From: ON DALLAS PARKWAY FROM LEBANON RD To: ELDORADO PKWY	ADDITION OF LANES	06/2022	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-24-265	0918-24-265	FRISCO	21037	VA	From: ON PANTHER CREEK PARKWAY FROM PRESTON ROAD To: DALLAS NORTH TOLLWAY	GRADE SEPARATION, NEW ROADWAY	01/2023	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-271	0918-47-271	GARLAND	14061	CS	From: ON SHILOH ROAD FROM KINGSLEY ROAD To: MILLER ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN	10/2023	09/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-289	0918-47-289	HIGHLAND PARK	14034	CS	From: ON WYCLIFF AVENUE FROM OAKLAWN AVENUE To: WEST OF GLENWOOD AVENUE	BRIDGE, RECONSTRUCTION, SAFETY	01/2024	12/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-45-812	0918-45-812	IRVING	11237.2	CS	From: ON CONFLANS RD FROM SH 161 To: VALLEY VIEW LANE	NEW ROADWAY, BIKE/PEDESTRIAN	06/2022	01/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0918-46-236	0918-46-236	LEWISVILLE	20131	CS From: ON CORPORATE DRIVE FROM ELM FORK TRINITY RIVER BRIDGE To: DGNO RR	ADDITION OF LANES, NEW ROADWAY	05/2022	10/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-46-326	0918-46-326	LEWISVILLE	20151	CS From: CORPORATE DR FROM RAILROAD STREET To: JOSEY LANE	ADDITION OF LANES, NEW ROADWAY	05/2022	10/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-46-237	0918-46-237	LEWISVILLE	20152	CS From: ON CORPORATE DRIVE To: AT ELM FORK TRINITY RIVER BRIDGE	ADDITION OF LANES, NEW ROADWAY	05/2022	12/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-46-238	0918-46-238	LEWISVILLE	20108	CS From: ON CORPORATE DR FROM HOLFORD'S PRAIRIE RD To: ELM FORK TRINITY RIVER BRIDGE	ADDITION OF LANES, NEW ROADWAY	12/2022	03/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-46-240	0918-46-240	LEWISVILLE	20113	CS From: ON CORPORATE DRIVE FROM FM 544 To: JOSEY LANE	ADDITION OF LANES, NEW ROADWAY	05/2022	12/2021	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-24-303	0918-24-303	LUCAS	20080	CS From: WEST LUCAS ROAD FROM COUNTRY CLUB (FM 1378) To: ANGEL PARKWAY (FM 2551)	ADDITION OF LANES, RECONSTRUCTION	03/2024	06/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0047-10-003	0047-10-003	MCKINNEY	21043	SP 399 From: SPUR 399 ALIGNMENT AT MCKINNEY NATIONAL AIRPORT To:	RECONSTRUCTION	10/2022	01/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE		PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0918-47-380	0918-47-380	NCTCOG	21044	VA	From: DALLAS INTERNATIONAL DISTRICT AUTOMATED TRANSPORTATION SYSTEM BOUNDED BY IH 635 TO THE SOUTH, DALLAS NORTH TOLLWAY To: TO THE WEST, PRESTON ROAD TO THE EAST, AND SPRING VALLEY ROAD TO THE NORTH	VEHICLE TECHNOLOGY	09/2023	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0000-02-045	0000-02-045	NCTCOG	25104.1	VA	From: SOUTH DALLAS IMPROVED BICYCLE/PEDESTRIAN ROUTES TO RAIL AND TRANSIT TECHNOLOGY UPGRADES To: BOUNDED BY BOTHAM JEAN BLVD TO THE NORTH, IH 45 TO THE EAST, IH 20 TO THE SOUTH, IH 35E TO THE WEST	BIKE/PEDESTRIAN	04/2025	06/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0000-18-104	0000-18-104	NTTA	84154	DNT	From: US 380 To: FM 428	NEW ROADWAY	04/2024	04/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0000-18-103	0000-18-103	NTTA	84153	DNT	From: SH 121 To: US 380	ADDITION OF LANES, RECONSTRUCTION	06/2022	08/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0000-18-107	0000-18-107	NTTA	84157	VA	From: PGBT-SH 360 CONNECTOR FROM PGBT (SH 161) To: SH 360/SUBLETT ROAD	NEW ROADWAY	06/2024	06/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0918-47-384	0918-47-384	ROWLETT	21077	CS	From: ON MERRITT ROAD FROM PRESIDENT GEORGE BUSH TURNPIKE To: CHIESA ROAD	BIKE/PEDESTRIAN, BRIDGE, NEW ROADWAY	02/2027	02/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0918-47-240	0918-47-240	SACHSE	14024	CS	From: ON MERRITT RD/WOODBRIDGE PKWY FROM PLEASANT VALLEY ROAD To: NORTH OF SACHSE ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN, INTERSECTION IMPROVEMENT, RECONSTRUCTION	01/2023	09/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0172-12-007	0172-12-007	TXDOT-DALLAS	14028	BUS 287S From: MCKINNEY STREET To: BRECKENRIDGE STREET	GRADE SEPARATION	09/2024	10/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0918-47-246	0918-47-246	TXDOT-DALLAS	14032	CS From: ON EAST BEAR CREEK ROAD FROM HAMPTON ROAD To: IH 35E	ADDITION OF LANES, BIKE/PEDESTRIAN, INTERSECTION IMPROVEMENT, RECONSTRUCTION	02/2025	08/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
1394-02-027	1394-02-027	TXDOT-DALLAS	13020	FM 1387 From: MIDLOTHIAN PARKWAY To: LONG BRANCH RD/BRYSON LANE	RECONSTRUCTION, ADDITION OF LANES	03/2026	08/2030	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0751-05-001	0751-05-001	TXDOT-DALLAS	83284	FM 148 From: SOUTH OF FM 3039 To: US 175	NEW ROADWAY	04/2023	06/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2679-03-016	2679-03-016	TXDOT-DALLAS	55037	FM 2514 From: NORTH OF DRAIN DRIVE To: BROWN STREET	ADDITION OF LANES	07/2022	07/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2679-03-015	2679-03-015	TXDOT-DALLAS	55038	FM 2514 From: EAST OF LAVON PARKWAY To: NORTH OF DRAIN DRIVE	ADDITION OF LANES	07/2022	07/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2056-01-042	2056-01-042	TXDOT-DALLAS	83209	FM 2551 From: FM 2514 To: FM 2170	ADDITION OF LANES	11/2023	04/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0816-02-072	0816-02-072	TXDOT-DALLAS	83255	FM 455 From: WEST OF FM 2450 To: EAST OF MARION RD	ADDITION OF LANES, RECONSTRUCTION	07/2022	07/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2588-02-008	2588-02-008	TXDOT-DALLAS	13017	FM 548 From: S OF SH 205 (KAUFMAN COUNTY LINE) To: SH 205	ADDITION OF LANES, RECONSTRUCTION	03/2026	03/2029	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2588-01-022	2588-01-022	TXDOT-DALLAS	55111.2	FM 548 From: NORTH OF US 80 To: WINDMILL FARMS BLVD	ADDITION OF LANES, RECONSTRUCTION	03/2026	03/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
1015-01-024	1015-01-024	TXDOT-DALLAS	83221	FM 549 From: SH 205 To: SH 276	ADDITION OF LANES	06/2026	06/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
1051-01-052	1051-01-052	TXDOT-DALLAS	13028	FM 664 From: FM 1387 To: WESTMORELAND ROAD	ADDITION OF LANES	07/2028	07/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
1051-01-051	1051-01-051	TXDOT-DALLAS	13035.1	FM 664 From: IH 35E To: WEST OF FERRIS ROAD	ADDITION OF LANES, RECONSTRUCTION	09/2025	09/2028	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
1051-03-001	1051-03-001	TXDOT-DALLAS	13035.2	FM 664 From: WEST OF FERRIS ROAD To: IH 45	ADDITION OF LANES, NEW ROADWAY	09/2027	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION		PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0009-12-219	0009-12-219	TXDOT-DALLAS	13036	IH 30	From: SH 205 To: WEST OF FM 2642 (HUNT COUNTY LINE)	ADDITION OF LANES, INTERCHANGE	11/2022	06/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0009-11-252	0009-11-252	TXDOT-DALLAS	13043.1	IH 30	From: IH 45 To: FERGUSON RD	RECONSTRUCTION, ADDITION OF LANES	09/2023	08/2032	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0009-12-220	0009-12-220	TXDOT-DALLAS	55195	IH 30	From: DALROCK To: EAST OF HORIZON	ADDITION OF LANES, INTERCHANGE, NEW ROADWAY, RECONSTRUCTION	10/2022	10/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0009-12-215	0009-12-215	TXDOT-DALLAS	55221	IH 30	From: DALROCK RD (DALLAS C/L) To: SH 205	ADDITION OF LANES	10/2022	08/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0009-11-248	0009-11-248	TXDOT-DALLAS	55253	IH 30	From: AT BASS PRO DRIVE To:	INTERCHANGE	09/2026	09/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0009-11-254	0009-11-254	TXDOT-DALLAS	13030	IH 30	From: IH 35E To: IH 45	ADDITION OF LANES, RECONSTRUCTION	02/2025	02/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0195-03-090	0195-03-090	TXDOT-DALLAS	13033.3	IH 35	From: IH 35W To: US 380	ADDITION OF LANES, INTERCHANGE, RECONSTRUCTION	09/2023	04/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0195-02-074	0195-02-074	TXDOT-DALLAS	55197	IH 35 From: US 77 (NORTH OF DENTON) To: SOUTH OF FM 455	ADDITION OF LANES, RECONSTRUCTION	12/2025	07/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0195-02-081	0195-02-081	TXDOT-DALLAS	55197.2	IH 35 From: NORTH OF FM 455 To: NORTH OF VIEW RD	ADDITION OF LANES, INTERSECTION IMPROVEMENT, RECONSTRUCTION	12/2024	12/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0195-02-084	0195-02-084	TXDOT-DALLAS	55197.3	IH 35 From: NORTH OF VIEW RD To: DENTON/COOKE CL	ADDITION OF LANES, RECONSTRUCTION	06/2024	11/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0195-03-087	0195-03-087	TXDOT-DALLAS	55198	IH 35 From: US 380 To: US 77 NORTH OF DENTON	ADDITION OF LANES, RECONSTRUCTION	09/2023	04/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0195-02-076	0195-02-076	TXDOT-DALLAS	55250	IH 35 From: AT FM 455 To:	ADDITION OF LANES, RECONSTRUCTION	07/2022	08/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0442-02-162	0442-02-162	TXDOT-DALLAS	54119.5	IH 35E From: ELLIS COUNTY LINE To: BEAR CREEK ROAD	INTERSECTION IMPROVEMENT	02/2023	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0442-03-044	0442-03-044	TXDOT-DALLAS	54119.6	IH 35E From: REESE DRIVE To: DALLAS COUNTY LINE	INTERCHANGE	09/2023	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0196-02-132	0196-02-132	TXDOT-DALLAS	55269	IH 35E From: FRANKFORD RD To: CORPORATE DR	BOTTLENECK REMOVAL	07/2022	12/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0196-02-126	0196-02-126	TXDOT-DALLAS	13033.4	IH 35E From: AT CORPORATE DRIVE To:	INTERCHANGE, RECONSTRUCTION	01/2025	01/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0195-03-099	0195-03-099	TXDOT-DALLAS	13033.6	IH 35E From: NORTH TEXAS BLVD To: IH 35W	ADDITION OF LANES, INTERCHANGE, RECONSTRUCTION	09/2023	04/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0442-03-042	0442-03-042	TXDOT-DALLAS	13034	IH 35E From: AT FM 664 To:	INTERCHANGE, RECONSTRUCTION	09/2023	02/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0442-02-161	0442-02-161	TXDOT-DALLAS	14032.2	IH 35E From: AT BEAR CREEK ROAD To:	BIKE/PEDESTRIAN, INTERSECTION IMPROVEMENT, RECONSTRUCTION	02/2025	02/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0196-02-128	0196-02-128	TXDOT-DALLAS	13033.1	IH 35E From: AT 1171 AND MAIN STREET To:	GRADE SEPARATION, RECONSTRUCTION	01/2023	01/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0196-02-127	0196-02-127	TXDOT-DALLAS	13033.2	IH 35E From: AT BS 121 To:	INTERCHANGE, RECONSTRUCTION	01/2025	01/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION		PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0196-01-109	0196-01-109	TXDOT-DALLAS	25033.3	IH 35E	From: SOUTH OF MAYHILL ROAD To: SOUTH OF SL 288	GRADE SEPARATION, INTERCHANGE, RECONSTRUCTION	06/2025	06/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0081-13-065	0081-13-065	TXDOT-DALLAS	55259	IH 35W	From: DALE EARNHARDT WAY To: FM 407	ADDITION OF LANES, RECONSTRUCTION	06/2025	06/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0092-03-053	0092-03-053	TXDOT-DALLAS	13029	IH 45	From: AT FM 664 To:	INTERCHANGE	09/2027	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2374-02-162	2374-02-162	TXDOT-DALLAS	53110.2	IH 635	From: AT US 80 INTERCHANGE To:	INTERCHANGE, RECONSTRUCTION	09/2026	07/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0353-09-003	0353-09-003	TXDOT-DALLAS	55260	SH 114	From: BUS 114K To: WEST OF US 377	NEW ROADWAY, RECONSTRUCTION	08/2025	08/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0353-02-037	0353-02-037	TXDOT-DALLAS	55235	SH 114	From: EAST OF IH 35W To: BUS 114K	NEW ROADWAY	08/2028	04/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0451-04-025	0451-04-025	TXDOT-DALLAS	55074.1	SH 205	From: JCT SH 205/JOHN KING (N. GOLIAD ST) To: NORTH OF JOHN KING (COLLIN COUNTY LINE)	ADDITION OF LANES	04/2026	04/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0451-05-003	0451-05-003	TXDOT-DALLAS	13038.1	SH 205 From: JCT SH 205/JOHN KING (S GOLIAD ST) To: JCT SH 205/JOHN KING (N GOLIAD ST)	RECONSTRUCTION	04/2026	04/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0451-03-013	0451-03-013	TXDOT-DALLAS	55073	SH 205 From: NORTH OF JOHN KING To: SH 78	ADDITION OF LANES	07/2022	07/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0091-03-022	0091-03-022	TXDOT-DALLAS	54023	SH 289 From: N BUS 289C, NORTH OF CELINA To: N CR 60/CR 107 (GRAYSON C/L)	ADDITION OF LANES	11/2025	08/2033	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0047-09-034	0047-09-034	TXDOT-DALLAS	13010	SH 5 From: SS 399 To: SOUTH OF FM 1378	ADDITION OF LANES, RECONSTRUCTION	06/2027	06/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0047-04-031	0047-04-031	TXDOT-DALLAS	13055	SH 5 From: SH 121 To: NORTH OF COLLIN COUNTY OUTER LOOP	ADDITION OF LANES, RECONSTRUCTION	11/2022	11/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0047-05-057	0047-05-057	TXDOT-DALLAS	13073	SH 5 From: STEWART RD To: ELDORADO PARKWAY	RECONSTRUCTION, ADDITION OF LANES	04/2025	04/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0047-04-032	0047-04-032	TXDOT-DALLAS	13021	SH 5 From: NORTH OF COLLIN COUNTY OUTER LOOP To: FM 455 WITH TRANSITIONAL SECTION/NORTH OF HACKBERRY DR	ADDITION OF LANES, RECONSTRUCTION	11/2024	08/2033	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0196-07-034	0196-07-034	TXDOT-DALLAS	14070	SS 366 From: WEST OF AKARD ST To: SAINT PAUL ST	ENHANCEMENT	01/2024	09/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0197-02-135	0197-02-135	TXDOT-DALLAS	21083.2	US 175 From: 2ND AVENUE To: SOUTH OF LAKE JUNE ROAD	ADDITION OF LANES, BIKE/PEDESTRIAN, BRIDGE	01/2024	03/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0197-03-078	0197-03-078	TXDOT-DALLAS	13077	US 175 From: WEST OF FM 148 BYPASS To: EAST OF FM 148 BYPASS	INTERCHANGE	04/2023	06/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0081-03-047	0081-03-047	TXDOT-DALLAS	20115	US 377 From: SOUTH OF FM 1171 To: CRAWFORD ROAD	ADDITION OF LANES	09/2027	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0135-04-033	0135-04-033	TXDOT-DALLAS	55234	US 380 From: 4TH STREET To: CR 458	ADDITION OF LANES	02/2024	05/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0135-03-046	0135-03-046	TXDOT-DALLAS	55233	US 380 From: WEST OF BRIDGEFARMER ROAD To: 4TH STREET	ADDITION OF LANES	02/2024	05/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0135-03-057	0135-03-057	TXDOT-DALLAS	55233.1	US 380 From: AIRPORT DRIVE To: WEST OF BRIDGEFARMER RD	ADDITION OF LANES	02/2024	05/2025	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0261-01-041	0261-01-041	TXDOT-DALLAS	55014	US 67 From: AT LAKE RIDGE PARKWAY To:	GRADE SEPARATION	03/2027	03/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0047-06-161	0047-06-161	TXDOT-DALLAS	13044	US 75 From: AT RIDGEVIEW DRIVE To:	INTERCHANGE, RECONSTRUCTION	06/2022	06/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0047-07-232	0047-07-232	TXDOT-DALLAS	30005	US 75 From: IH 635 To: COLLIN COUNTY LINE	HOV/MANAGED/EXPRESS, SAFETY	12/2022	08/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0047-06-158	0047-06-158	TXDOT-DALLAS	30006	US 75 From: DALLAS COUNTY LINE To: BETHANY DRIVE	HOV/MANAGED/EXPRESS, SAFETY	12/2022	08/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0047-06-163	0047-06-163	TXDOT-DALLAS	30007	US 75 From: BETHANY DRIVE To: SH 121	ADDITION OF LANES, HOV/MANAGED/EXPRESS	12/2022	08/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0047-14-053	0047-14-053	TXDOT-DALLAS	20084	US 75 From: NORTH OF CR 370 To: CR 375 (GRAYSON COUNTY LINE)	ADDITION OF LANES, RECONSTRUCTION	09/2026	01/2024	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0095-02-096	0095-02-096	TXDOT-DALLAS	53110	US 80 From: EAST OF BELT LINE RD To: LAWSON RD	ADDITION OF LANES, RECONSTRUCTION	09/2025	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.


**EXHIBIT IV-2 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL START	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0095-03-080	0095-03-080	TXDOT-DALLAS	53086	US 80 From: LAWSON ROAD (DALLAS/KAUFMAN C/L) To: FM 460	ADDITION OF LANES	11/2022	06/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0095-02-107	0095-02-107	TXDOT-DALLAS	53109	US 80 From: EAST OF TOWN EAST BLVD To: EAST OF BELT LINE RD	ADDITION OF LANES, INTERCHANGE, RECONSTRUCTION	09/2026	07/2024	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
1068-04-170	1068-04-170	TXDOT-FORT WORTH	13000	IH 30 From: DALLAS COUNTY LINE To: SH 161	ADDITION OF LANES, RECONSTRUCTION	09/2026	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

Chapter IV Project Implementation/Progress from Previous Years

Roadway – Paris District

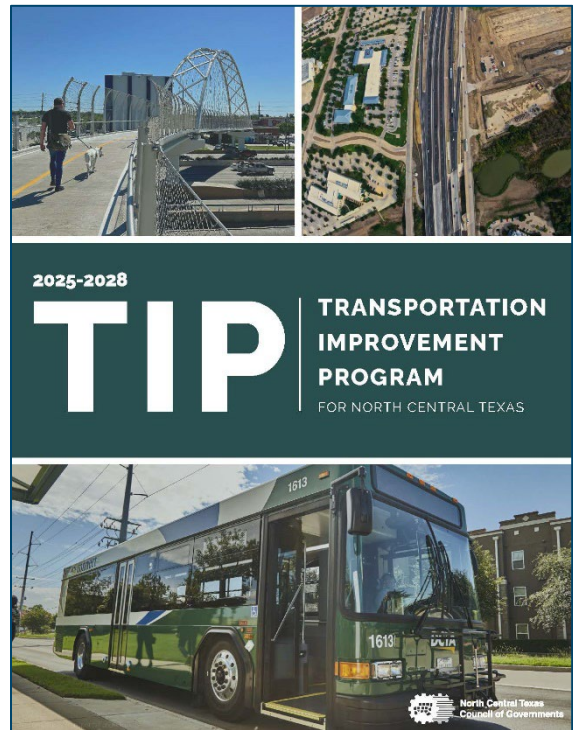

**EXHIBIT IV-3 - TXDOT PARIS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION		PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
2659-01-010	2659-01-010	TXDOT-PARIS	13052	FM 1570	From: IH 30 To: SH 66	ADDITION OF LANES	09/2026	09/2027	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2658-01-013	2658-01-013	TXDOT-PARIS	13039	FM 2642	From: FM 35 To: SH 66	ADDITION OF LANES, BIKE/PEDESTRIAN	10/2022	01/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0009-13-168	0009-13-168	TXDOT-PARIS	55224	IH 30	From: EAST OF FM 1565 To: EAST OF FM 36	GRADE SEPARATION, INTERCHANGE, RECONSTRUCTION	05/2023	10/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0009-13-169	0009-13-169	TXDOT-PARIS	55225	IH 30	From: EAST OF CR 2511 To: EAST OF FM 1565	INTERCHANGE, RECONSTRUCTION	05/2023	10/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0009-13-170	0009-13-170	TXDOT-PARIS	55226	IH 30	From: WEST OF CR 2511 To: EAST OF CR 2511	INTERCHANGE	05/2023	10/2023	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
0009-13-175	0009-13-175	TXDOT-PARIS	21051	IH 30	From: AT MONTY STRATTON PARKWAY To:	ADDITION OF LANES, INTERCHANGE	10/2022	10/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0009-13-174	0009-13-174	TXDOT-PARIS	13065	IH 30	From: FM 2642 To: MONTY STRATTON PARKWAY	RECONSTRUCTION	09/2026	09/2026	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.


**EXHIBIT IV-3 - TXDOT PARIS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
ROADWAY SECTION PROJECTS**

ORIGINAL CSJ	REVISED CSJ	AGENCY	TIP CODE	PROJECT LOCATION	PROJECT TYPE	ORIGINAL LET DATE	REVISED LET DATE	LET	COMPLETED	DELAYED	CANCELLED
0009-13-173	0009-13-173	TXDOT-PARIS	55223	IH 30 From: WEST OF FM 1903 To: EAST OF FM 1903	INTERCHANGE, RECONSTRUCTION	10/2022	10/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
0009-13-167	0009-13-167	TXDOT-PARIS	13050	IH 30 From: AT FM 1570 To:	INTERCHANGE	10/2022	10/2022	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

NOTE: No checkmark, means the project was in the 2023-2026 TIP and is in the 2025-2028 TIP with the same schedule or was advanced to an earlier schedule.

Chapter IV Project Implementation/Progress from Previous Years

Transit – Fort Worth District

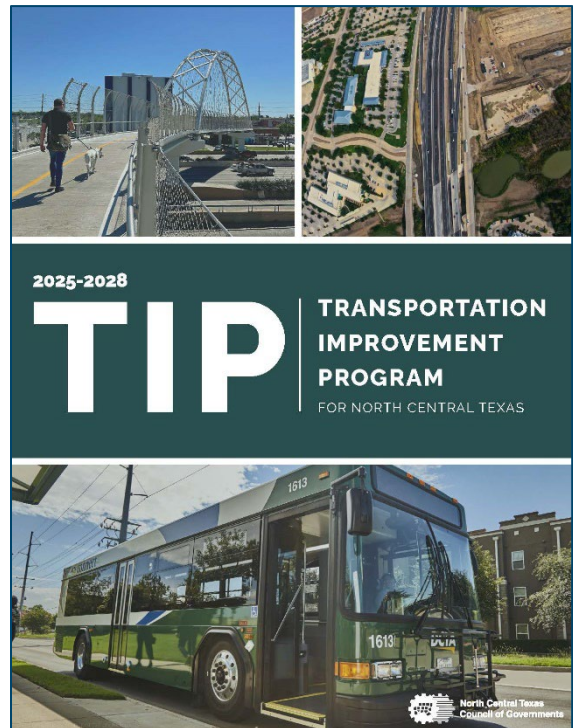

**EXHIBIT IV-4 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
City of Arlington	12037.2	OPERATING ASSISTANCE	OPERATING	2022	Section 5307
City of Arlington	12904.2	CAPITAL COST OF CONTRACTING - VIA	CAPITAL	2022	Section 5307
City of Arlington	12906.2	CAPITAL COST OF CONTRACTING - HANDITRAN	CAPITAL	2022	Section 5307
City of Arlington	12907.2	PREVENTIVE MAINTENANCE	CAPITAL	2022	Section 5307
City of Arlington	12904.21	CAPITAL COST OF CONTRACTING - VIA	CAPITAL	2023	Section 5307
City of Arlington	12906.21	CAPITAL COST OF CONTRACTING - HANDITRAN	CAPITAL	2023	Section 5307
City of Arlington	12907.21	PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
City/County	12871.21	MOBILITY MANAGEMENT	CAPITAL	2023	Section 5307
City/County	12782.21	PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
City/County	12781.21	ACQUISITION OF SIGNAGE	CAPITAL	2023	Section 5307

* Funding Categories are referenced by Section Number in listing, but are defined as:

5307 - Urbanized Area Formula Program

5309 - Fixed Guideway Capital Investment Grant Program

5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program

5311 - Non-Urbanized Area Formula Program

5312 - Mobility On-Demand Demo

5339 - Bus & Bus Facilities Program

**EXHIBIT IV-4 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
City/County	12748.22	ACQUISITION OF SOFTWARE	CAPITAL	2024	Section 5307
City/County	12750.22	PROJECT ADMINISTRATION	CAPITAL	2024	Section 5307
Fort Worth Transportation Authority	25072.3	REPLACE BRIDGES AT WALKERS CREEK AND MESQUITE CREEK; AND CONSTRUCT 2.4 MILES OF NEW SECOND TRACK FROM EAST OF HANDLEY EDERVILLE ROAD TO EAST OF PRECINCT LINE ROAD	CAPITAL	2022	BUILD
Fort Worth Transportation Authority	12982.21	EMERGENCY OPERATING ASSISTANCE - 100% FEDERAL SHARE	OPERATING	2023	ARP/Section 5310
Fort Worth Transportation Authority	11543.4	EMERGENCY OPERATING ASSISTANCE - 100% FEDERAL SHARE	OPERATING	2023	CRRSAA/Section 5307
Fort Worth Transportation Authority	12549.21	ADA PARATRANSIT SERVICE	CAPITAL	2023	Section 5307
Fort Worth Transportation Authority	12038.22	SYSTEM PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
Fort Worth Transportation Authority	12038.21	SYSTEM PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
Fort Worth Transportation Authority	12947.21	TCTS PURCHASE OF SERVICE	CAPITAL	2023	Section 5310
Fort Worth Transportation Authority	12462.21	RAIL PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5337

* Funding Categories are referenced by Section Number in listing, but are defined as:

- 5307 - Urbanized Area Formula Program
- 5309 - Fixed Guideway Capital Investment Grant Program
- 5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program
- 5311 - Non-Urbanized Area Formula Program
- 5312 - Mobility On-Demand Demo
- 5339 - Bus & Bus Facilities Program

**EXHIBIT IV-4 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
Fort Worth Transportation Authority	12462.22	RAIL PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5337
Fort Worth Transportation Authority	12928.2	COMPREHENSIVE PAYMENT SYSTEM	CAPITAL	2023	Section 5339
Fort Worth Transportation Authority	11176.7	REGIONAL VANPOOL PROGRAM FOR WESTERN SUBREGION	CAPITAL	2023	STBG
North Central Council of Governments	25089.2	DEVP & IMPL OF A RRS TO ASST W/ FREIGHT & PASS TRAIN DEVP & IMPL A RRS TO ASSIST W/ FREIGHT & PASS TRAIN INTERACTIONS; INCR PLANNED FREIGHT & PASS RAIL GRWTH, IDENTIFY RAIL BOTTLENECKS & ENHANCE LNG TERM MOB PLN PROJ INCL. CONSULT & STAFF ACTIVITIES	CAPITAL	2022	BUILD
North Central Council of Governments	12678.21	PROGRAM ADMINISTRATION	CAPITAL	2022	Section 5310
North Central Council of Governments	12018.21	GENERAL PLANNING	CAPITAL	2023	APP/Section 5307
North Central Council of Governments	12736.2	PURCHASE REPLACEMENT VEHICLES	CAPITAL	2023	Section 5339
North Central Council of Governments	12793.2	PROJECT ADMINISTRATION	CAPITAL	2023	Section 5339
North Central Council of Governments	12779.22	MOBILITY MANAGEMENT - STRATEGIC PARTNERSHIP	CAPITAL	2024	Section 5310
North Central Council of Governments	12678.22	PROGRAM ADMINISTRATION	CAPITAL	2024	Section 5310

* Funding Categories are referenced by Section Number in listing, but are defined as:

5307 - Urbanized Area Formula Program

5309 - Fixed Guideway Capital Investment Grant Program

5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program

5311 - Non-Urbanized Area Formula Program

5312 - Mobility On-Demand Demo

5339 - Bus & Bus Facilities Program

**EXHIBIT IV-4 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
North Central Council of Governments	12793.21	PROJECT ADMINISTRATION	CAPITAL	2024	Section 5339
Northeast Transportation Services	12600.2	CAPITAL COST OF CONTRACTING	CAPITAL	2022	Section 5307
Northeast Transportation Services	12653.21	PURCHASE OF SERVICE	CAPITAL	2023	Section 5310
Northeast Transportation Services	12966.21	PURCHASE OF REPLACEMENT VEHICLES	CAPITAL	2023	Section 5310
Northeast Transportation Services	12965.21	PURCHASE OF EXPANSION VEHICLES	CAPITAL	2023	Section 5310
Northeast Transportation Services	12600.2	CAPITAL COST OF CONTRACTING	CAPITAL	2024	Section 5307
Public Transit Service	12246.21	OPERATING ASSISTANCE	CAPITAL	2023	ARP/Section 5307
Public Transit Service	12666.21	MOBILITY MANAGEMENT	CAPITAL	2023	Section 5307
Public Transit Service	12666.22	MOBILITY MANAGEMENT	CAPITAL	2024	Section 5307
Public Transit Service	12247.22	PROJECT ADMINISTRATION	CAPITAL	2024	Section 5307

* Funding Categories are referenced by Section Number in listing, but are defined as:

- 5307 - Urbanized Area Formula Program
- 5309 - Fixed Guideway Capital Investment Grant Program
- 5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program
- 5311 - Non-Urbanized Area Formula Program
- 5312 - Mobility On-Demand Demo
- 5339 - Bus & Bus Facilities Program

**EXHIBIT IV-4 - TXDOT FORT WORTH
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**


AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
Public Transit Service	12696.22	PREVENTIVE MAINTENANCE	CAPITAL	2024	Section 5307

* Funding Categories are referenced by Section Number in listing, but are defined as:

- 5307 - Urbanized Area Formula Program
- 5309 - Fixed Guideway Capital Investment Grant Program
- 5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program
- 5311 - Non-Urbanized Area Formula Program
- 5312 - Mobility On-Demand Demo
- 5339 - Bus & Bus Facilities Program

Chapter IV Project Implementation/Progress from Previous Years

Transit – Dallas District

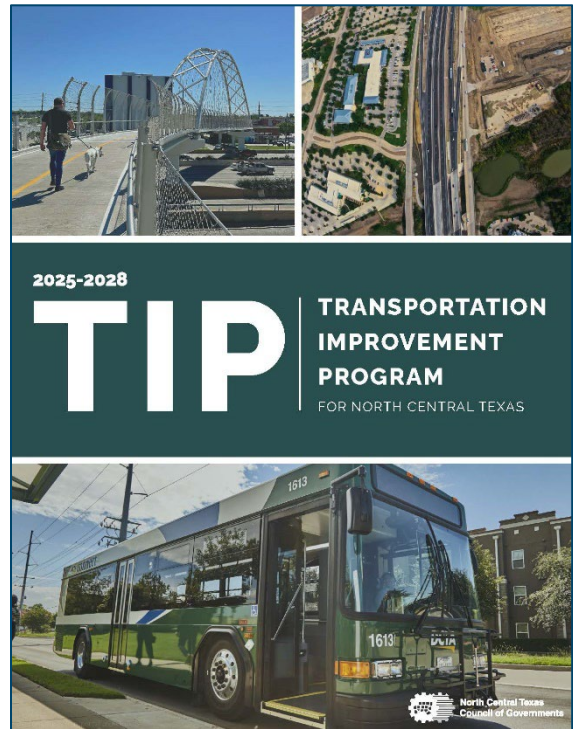

**EXHIBIT IV-5 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
City of Grand Prairie	12650.2	OPERATING ASSISTANCE (SPECIAL RULE)	OPERATING	2022	Section 5310
CITY OF GRAND PRAIRIE	12078.23	REHAB/RENOVATION ADP HARDWARE	CAPITAL	2023	FHWA
City of Grand Prairie	12078.23	REHAB/RENOVATION ADP HARDWARE	CAPITAL	2023	Section 5307
Community Transit Services	12010.22	ACQUISITION OF HARDWARE	CAPITAL	2024	Section 5307
Community Transit Services	12019.22	ACQUISITION OF STORAGE SHED	CAPITAL	2024	Section 5307
Community Transit Services	12020.22	ACQUISITION OF SOFTWARE	CAPITAL	2024	Section 5307
Community Transit Services	12860.22	ACQUISITION OF SECURITY EQUIPMENT	CAPITAL	2024	Section 5307
Dallas Area Rapid Transit	25072.1	REHAB EXISTING BRIDGE OVER INWOOD ROAD AND ADD ADJACENT BRIDGE FOR NEW SECOND TRACK; ADD NEW BRIDGE AT KNIGHTS BRANCH FOR A NEW SECOND TRACK; REPLACE CURRENT NOBLE BRANCH BRIDGE AND ADD ADJACENT BRIDGE FOR SECOND TRACK	CAPITAL	2022	CAT 3 BUILD GRANT
Dallas Area Rapid Transit	12028.21	SYSTEM PREVENTIVE MAINTENANCE	CAPITAL	2022	Section 5307
Dallas Area Rapid Transit	12937.19	HUMAN TRAFFICKING AWARENESS PROGRAM	CAPITAL	2022	Section 5312

* Funding Categories are referenced by Section Number in listing, but are defined as:

- 5307 - Urbanized Area Formula Program
- 5309 - Fixed Guideway Capital Investment Grant Program
- 5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program
- 5311 - Non-Urbanized Area Formula Program
- 5312 - Mobility On-Demand Demo
- 5339 - Bus & Bus Facilities Program

**EXHIBIT IV-5 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
Dallas Area Rapid Transit	12471.21	RAIL PREVENTIVE MAINTENANCE	CAPITAL	2022	Section 5337
Dallas Area Rapid Transit	14013.5	CONSTRUCT NEW SHARED-USE PATH BRIDGE AT EAST PLANO PARKWAY	CAPITAL	2022	TA SET-ASIDE CFP
Dallas Area Rapid Transit	12028.22	SYSTEM PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
Dallas Area Rapid Transit	12838.17	RED AND BLUE LINE PLATFORM EXTENSION	CAPITAL	2023	Section 5309
Dallas Area Rapid Transit	12471.22	RAIL PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5337
Dallas Area Rapid Transit	12928.2	COMPREHENSIVE PAYMENT SYSTEM	CAPITAL	2023	Section 5339
Dallas Area Rapid Transit	14013.2	DESIGN FOR COTTON BELT VELOWEB TRAIL (26 MILES) AND CONSTRUCTION OF MULTIPLE SECTIONS OF THE TRAIL CORRIDOR (IN COPPELL, CARROLLTON, ADDISON, DALLAS, PLANO, AND RICHARDSON)	CAPITAL	2024	FHWA
Denton County Transportation Authority	12354.21	ACQUISITION OF SECURITY EQUIPMENT	CAPITAL	2023	Section 5307
Denton County Transportation Authority	12416.21	SYSTEM PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
Denton County Transportation Authority	12356.21	ADA PARATRANSIT SERVICE	CAPITAL	2023	Section 5307

* Funding Categories are referenced by Section Number in listing, but are defined as:

5307 - Urbanized Area Formula Program

5309 - Fixed Guideway Capital Investment Grant Program

5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program

5311 - Non-Urbanized Area Formula Program

5312 - Mobility On-Demand Demo

5339 - Bus & Bus Facilities Program

**EXHIBIT IV-5 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
Denton County Transportation Authority	12465.21	OPERATING ASSISTANCE (SPECIAL RULE)	OPERATING	2023	Section 5307
Denton County Transportation Authority	12909.21	RAIL PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5337
Denton County Transportation Authority	12745.2	SWIFTLY TRANSIT PLATFORM	CAPITAL	2023	Section 5339
Denton County Transportation Authority	21015.4	ACTIVITIES TO PRESERVE AND EXTEND THE FUNCTIONALITY AND SERVICEABILITY OF CAPITAL ASSETS	CAPITAL	2023	STBG
Denton County Transportation Authority	12996.21	MOBILITY MANAGEMENT	CAPITAL	2024	ARP/Section 5310
Denton County Transportation Authority	12009.22	MOBILITY MANAGEMENT	CAPITAL	2024	CRRSAA/Section 5310
Denton County Transportation Authority	11639.1	OPERATE A VANPOOL SUBSIDY INITIATIVE FOR COMMUTERS TRAVELING LONG DISTANCES AND IN AREAS WITH LITTLE OR NO FIXED ROUTE SERVICE	CAPITAL	2024	STBG
North Central Council of Governments	12004.21	COMPREHENSIVE PLANNING STUDY FOR TRANSIT-ORIENTED DEVELOPMENT AT NINE DART SILVER LINE REGIONAL RAIL STATIONS	CAPITAL	2022	Section 5309 TOD
North Central Council of Governments	12677.21	PROGRAM ADMINISTRATION	CAPITAL	2022	Section 5310
North Central Council of Governments	12989.18	GENERAL PLANNING	CAPITAL	2023	Section 5307

* Funding Categories are referenced by Section Number in listing, but are defined as:

- 5307 - Urbanized Area Formula Program
- 5309 - Fixed Guideway Capital Investment Grant Program
- 5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program
- 5311 - Non-Urbanized Area Formula Program
- 5312 - Mobility On-Demand Demo
- 5339 - Bus & Bus Facilities Program

**EXHIBIT IV-5 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
North Central Council of Governments	12542.21	SUPPORT URBANIZED AREA TRANSIT SERVICE	CAPITAL	2023	Section 5307
North Central Council of Governments	12005.21	GENERAL PLANNING	CAPITAL	2023	Section 5307
North Central Council of Governments	12783.21	PURCHASE EXPANSION VEHICLES	CAPITAL	2023	Section 5307
North Central Council of Governments	12870.21	MOBILITY MANAGEMENT	CAPITAL	2023	Section 5307
North Central Council of Governments	12205.21	PROJECT ADMINISTRATION	CAPITAL	2023	Section 5307
North Central Council of Governments	12737.22	MOBILITY MANAGEMENT - STRATEGIC PARTNERSHIP	CAPITAL	2024	Section 5310
North Central Council of Governments	12677.22	PROGRAM ADMINISTRATION	CAPITAL	2024	Section 5310
North Central Council of Governments	12796.21	PURCHASE EXPANSION VEHICLES	CAPITAL	2024	Section 5339
Span, Inc.	12919.21	PURCHASE OF SERVICE - THE COLONY	CAPITAL	2022	Section 5310
Span, Inc.	12920.21	PURCHASE OF SERVICE - LITTLE ELM	CAPITAL	2022	Section 5310

* Funding Categories are referenced by Section Number in listing, but are defined as:

5307 - Urbanized Area Formula Program

5309 - Fixed Guideway Capital Investment Grant Program

5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program

5311 - Non-Urbanized Area Formula Program

5312 - Mobility On-Demand Demo

5339 - Bus & Bus Facilities Program

**EXHIBIT IV-5 - TXDOT DALLAS
PROJECT IMPLEMENTATION/PROGRESS FROM PREVIOUS YEARS
TRANSIT SECTION PROJECTS**

AGENCY	TIP CODE	PROJECT DESCRIPTION	WORK TYPE	GRANT FISCAL YEAR	FUNDING CATEGORY*
Span, Inc.	12150.21	OPERATING ASSISTANCE (SPECIAL RULE)	OPERATING	2023	Section 5307
Span, Inc.	12711.21	MOBILITY MANAGEMENT	CAPITAL	2023	Section 5307
Span, Inc.	12714.21	ACQUISITION OF SIGNAGE	CAPITAL	2023	Section 5307
Span, Inc.	12625.21	PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307
Span, Inc.	12711.22	MOBILITY MANAGEMENT	CAPITAL	2024	Section 5307
Span, Inc.	12375.22	PROJECT ADMINISTRATION	CAPITAL	2024	Section 5307
STAR Transit	12704.21	PURCHASE OF SERVICE	CAPITAL	2022	Section 5310
STAR Transit	12151.21	OPERATING ASSISTANCE	CAPITAL	2023	ARP/Section 5307
STAR Transit	12717.21	MOBILITY MANAGEMENT	CAPITAL	2023	Section 5307
STAR Transit	12627.21	PREVENTIVE MAINTENANCE	CAPITAL	2023	Section 5307

* Funding Categories are referenced by Section Number in listing, but are defined as:

5307 - Urbanized Area Formula Program

5309 - Fixed Guideway Capital Investment Grant Program

5310 - Enhanced Mobility of Seniors & Individuals with Disabilities Program

5311 - Non-Urbanized Area Formula Program

5312 - Mobility On-Demand Demo

5339 - Bus & Bus Facilities Program
